

TECH CONSTRUCTION PROGRESS

4/11/18


WORK IN PLACE THROUGH MARCH

- Footings and Foundations in place in the three Learning Neighborhoods, Commons, Gymnasium, Performing Arts Area, and underway in the Pool/Locker-room Spaces.
- Structural Steel installation continues in the Learning Neighborhoods.
- Metal Stud wall framing is underway in Learning Neighborhood 1.
- Precast Wall Panel installation is 90% complete at the Gymnasium with Masonry work underway
- Masonry wall install continues at elevator shafts and interior walls.

FOOTING AND FOUNDATION COMPLETION



Footings and Foundations Continue

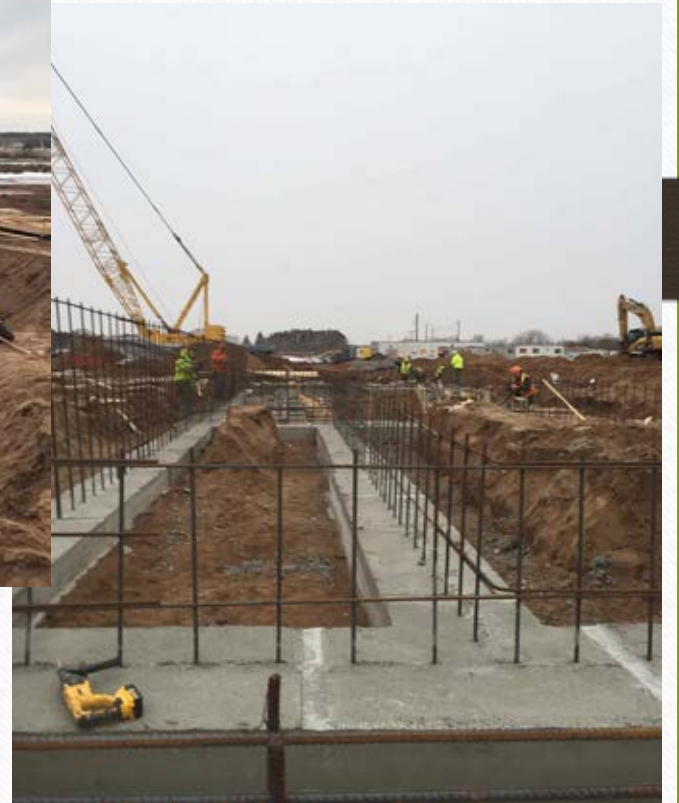

Structural Steel Installation and Elevator Shaft



Exterior Wall Framing Installation Underway



Structural Steel Installation



Precast Wall Panel Installation



Gymnasium and Learning Neighborhood Progress



Overall Site View



UPCOMING SCHEDULED ACTIVITIES

- Footings and Foundations to continue in Pool, and Administration Areas.
- Structural Steel installation to continue in the Commons, Gym and Pool
- Load Bearing Masonry to begin in the Locker rooms.
- Exterior Wall Framing to continue in the Learning Neighborhoods along with wall sheathing in Area 1
- Underground Plumbing to begin in Area 1.
- Roofing to begin in Area 1.
- Box Culvert Installation is set to begin around April 30th. Planned for 2 weeks of installation to be followed by the road installation (2-3 weeks)
