

# TECH CONSTRUCTION PROGRESS

12/6/17



# WORK IN PLACE THROUGH DEC 5<sup>th</sup>

---

- Footings and Foundations in place in Areas 1, 2, 3 and 4
- Sanitary Sewer lift station is in place along with a portion of the water lines
- Area 7 (Performing Arts) footings excavated and rebar installation underway.
  - Scheduled to pour concrete in these footings this week
- Mass site grading completed for the year.



# Sanitary Sewer Lift Station



Details: Bottom of the Lift Station is 25' below the building floor and sitting on the bedrock.



# Sanitary Sewer Lift Station



Details: Bottom of the Lift Station is 25' below the building floor and sitting on the bedrock.



# Footings and Foundations Continue






Footings Poured  
Foundations Poured





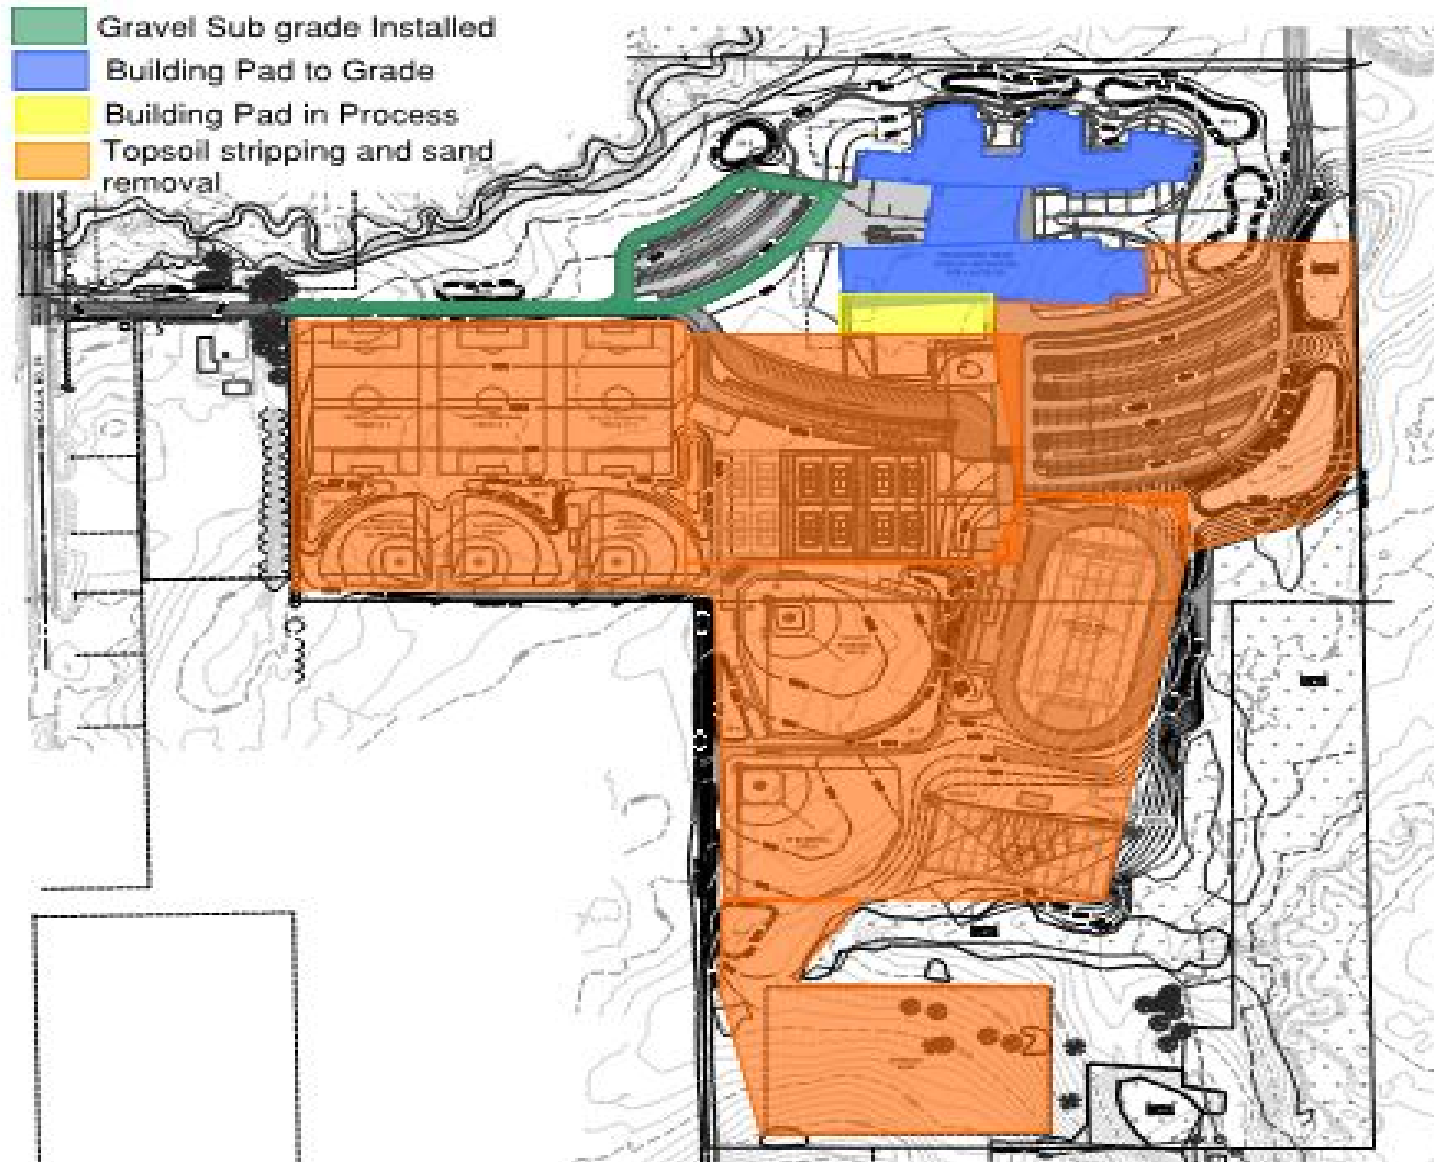















# UPCOMING SCHEDULED ACTIVITIES

---

- Footings and Foundations to continue in Areas 5, 6, 7 and 8.
- Continue sewer and water work through this week.
- Structural Steel installation to begin on January 16<sup>th</sup>.
- Precast Wall Panels to begin being installed at the Gymnasium on February 26<sup>th</sup>.
- Bid Package 3 Bid Opening on December 21<sup>st</sup> at 2:00, St Cloud City Hall.
